

I-90 Two Way Transit & HOV Operations

Stage 3 on Mercer Island

Russ East

WSDOT Asst. Regional Administrator

Paula Hammond

Secretary of Transportation

Steve Reinmuth

Chief of Staff

Jan. 7, 2013

Mercer Island City Council

I-90 Two Way Transit and HOV Operations

Stage 3 Overview

- Add HOV lanes to I-90 between Seattle and Bellevue
- Build and modify existing HOV direct access ramps on Mercer Island
- Modify existing HOV direct access ramps at Bellevue Way



Project Timeline

Construction in 3 stages

Stage 1

New HOV lane westbound and direct-access ramps between Mercer Island and Bellevue.

Completed 2008

Stage 2

New HOV lane eastbound, direct access ramps between Bellevue and Mercer Island

Complete: early 2012

Stage 3

New HOV lanes both directions, Seattle-Mercer Island; tunnel fire-safety upgrade.

Construction: August 2014
Complete: September 2016





Stage Progress

80th Ave. SE to Rainier Ave.



Bellevue Way to 80th Ave. SE

2007





Stage 1
complete
Oct. 2008

2009



Stage 2
complete
March 2012

2012



Stage 3
complete
Sept. 2016

2016




2022/2023




I-90 Two-Way Transit & HOV Operations

I-90 Homer M. Hadley Bridge at completion of East Link

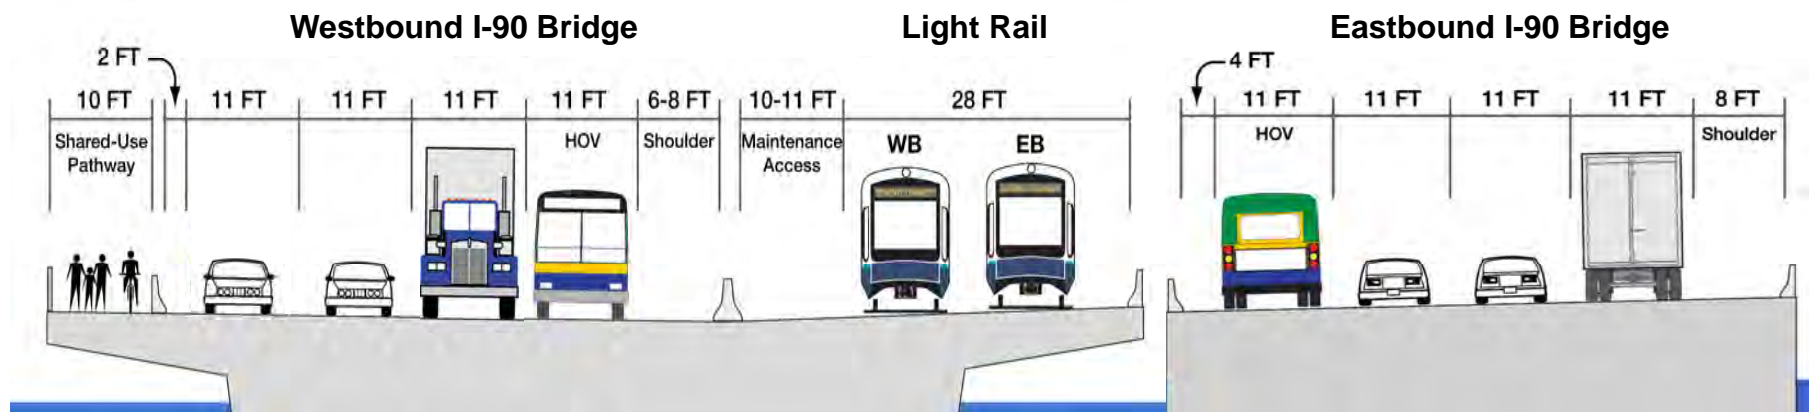

Total cost estimate fluctuation

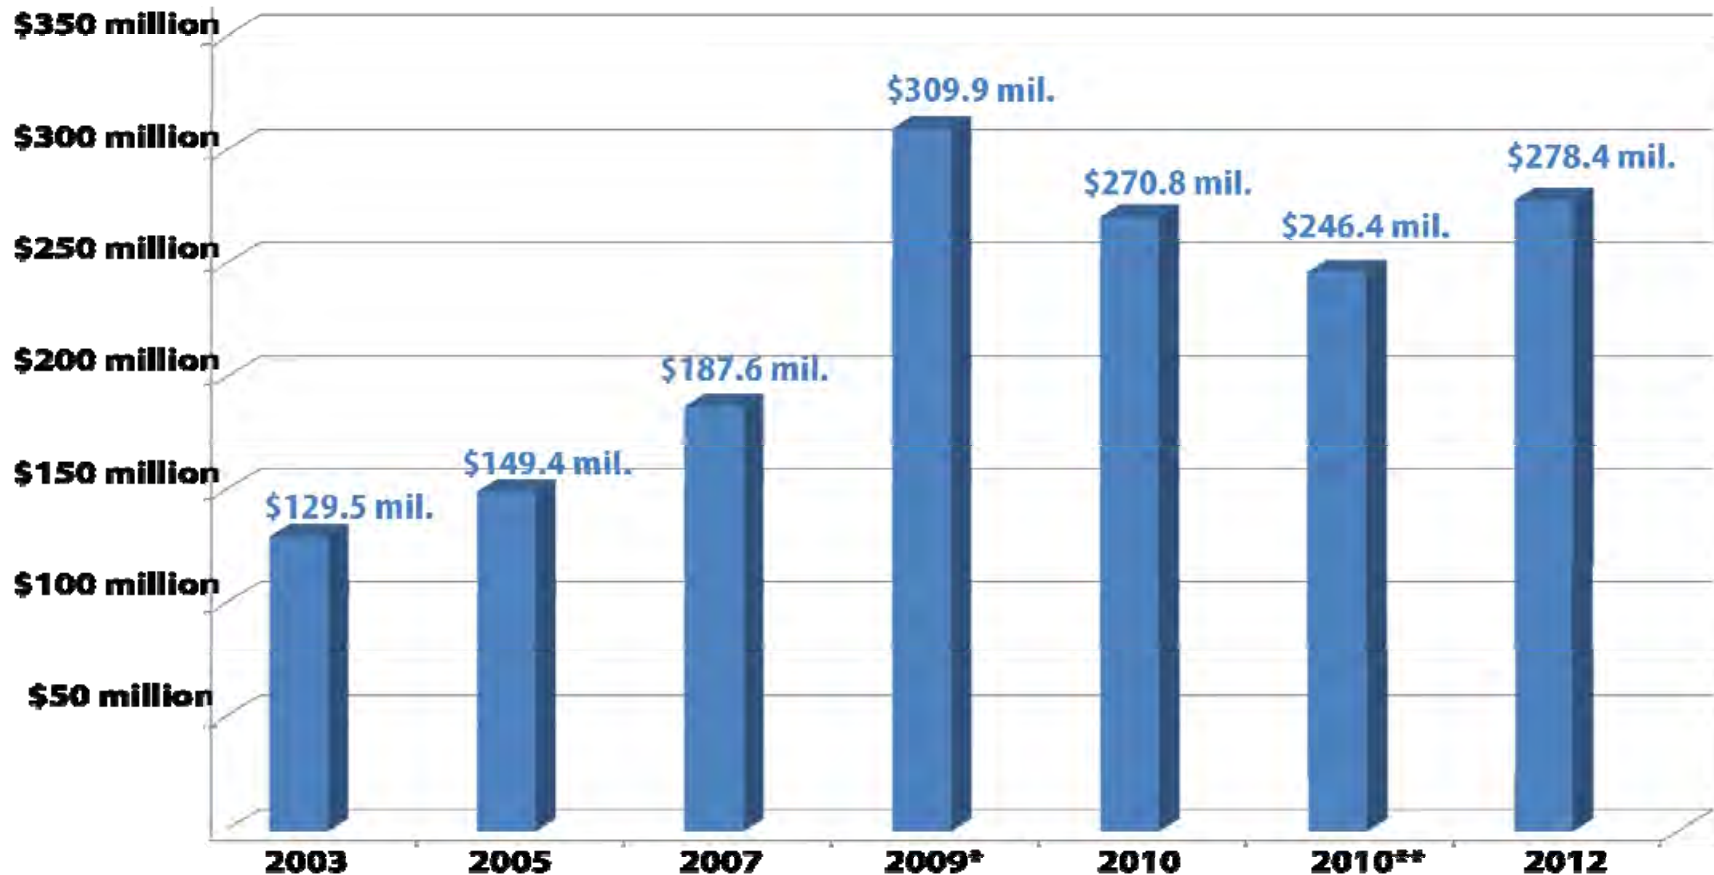

Changes in total project cost estimates by year based on Cost Estimate and Validation Process (CEVP).

*2009 estimate based on consultant Type Size & Location process (TS&L).

**2010 estimate reflects mitigated CEVP.
